


FAILURE TO FOLLOW THE SEQUENCE OF CONSTRUCTION OF THE APPROVED PLAN SHALL BE CONSIDERED A VIOLATION AND WILL RESULT IN FURTHER ENFORCEMENT, INCLUDING, BUT NOT LIMITED TO, STOP WORK ORDERS AND CIVIL PENALTIES.

1. PRIOR TO ANY LAND DISTURBING ACTIVITY, INCLUDING CLEARING, GRUBBING, DEMOLITION AND/OR GRADING OPERATIONS, THE CONTRACTOR SHALL INSTALL ALL PROPOSED PERIMETER EROSION AND SEDIMENT CONTROL MEASURES INCLUDING CONSTRUCTION ENTRANCES, SILT FENCE, CULVERT INLET PROTECTION, AND INLET PROTECTION ALONG HAMMON BLVD. IT IS RECOMMENDED THAT THE CONTRACTOR HAVE WA81 MARK THE LOCATION OF ANY AND ALL EXISTING UTILITIES TO AVOID POTENTIAL SEVERING OF SERVICE. THE CONTRACTOR SHALL INSTALL THE PERIMETER EROSION AND SEDIMENT CONTROL MEASURES PER THE APPROVED PLAN.
2. UPON PROPER ESTABLISHMENT OF PERIMETER CONTROLS AND APPROVAL BY THE TOWN INSPECTOR, THE CONTRACTOR CAN BEGIN DEMOLITION, STRIPPING AND STOCKPILING OF TOPSOIL, CLEARING AND GRUBBING AND GRADING OPERATIONS. THE UPPER PORTION OF THE SITE WHERE THE BARRIERS AND INLET PROTECTION SHALL BE INSPECTED IMMEDIATELY AFTER EACH RAINFALL EVENT AND AT LEAST DAILY DURING PROLONGED RAINFALL. ANY NECESSARY REPAIRS SHALL BE COMPLETED IMMEDIATELY. SEDIMENT DEPOSITS SHALL BE REMOVED AFTER EACH STORM EVENT.
3. UPON ACHIEVING SUBGRADE ELEVATIONS, AND STABILIZATION OF ALL UPSTREAM AREAS, CONTRACTOR SHALL NOTIFY TOWN STAFF PRIOR TO CONSTRUCTION OF THE STORM WATER MANAGEMENT FACILITY, STORM PIPE AND PERIMETER DITCH. INLET PROTECTION SHALL BE ADDED TO THE DI-1 AFTER INSTALLATION.
4. ONCE POND AND STORMWATER FEATURES SUCH AS PIPING AND INLETS ARE COMPLETED, THE STORM WATER FACILITY SHALL BE SEEDED AND STABILIZED.
5. THE CONTRACTOR SHALL CONTACT TOWN OF CHRISTIANSBURG ENGINEERING DEPARTMENT TO OBTAIN THE FINAL SITE INSPECTION. UPON SATISFACTION OF SEEDING AND AGREEMENT WITH TOWN STAFF TEMPORARY SEDIMENT CONTROL MEASURES MAY BE REMOVED.

DURING CONSTRUCTION	FINAL CONDITION

* LIMITS OF DISTURBANCE SHALL BE CLEARLY MARKED ON SITE WITH PAINT, STAKES, OR OTHER METHOD. ACCEPTABLE MARKINGS SHALL BE COORDINATED WITH THE TOWN OF CHRISTIANBURG INSPECTIONS PERSONNEL.

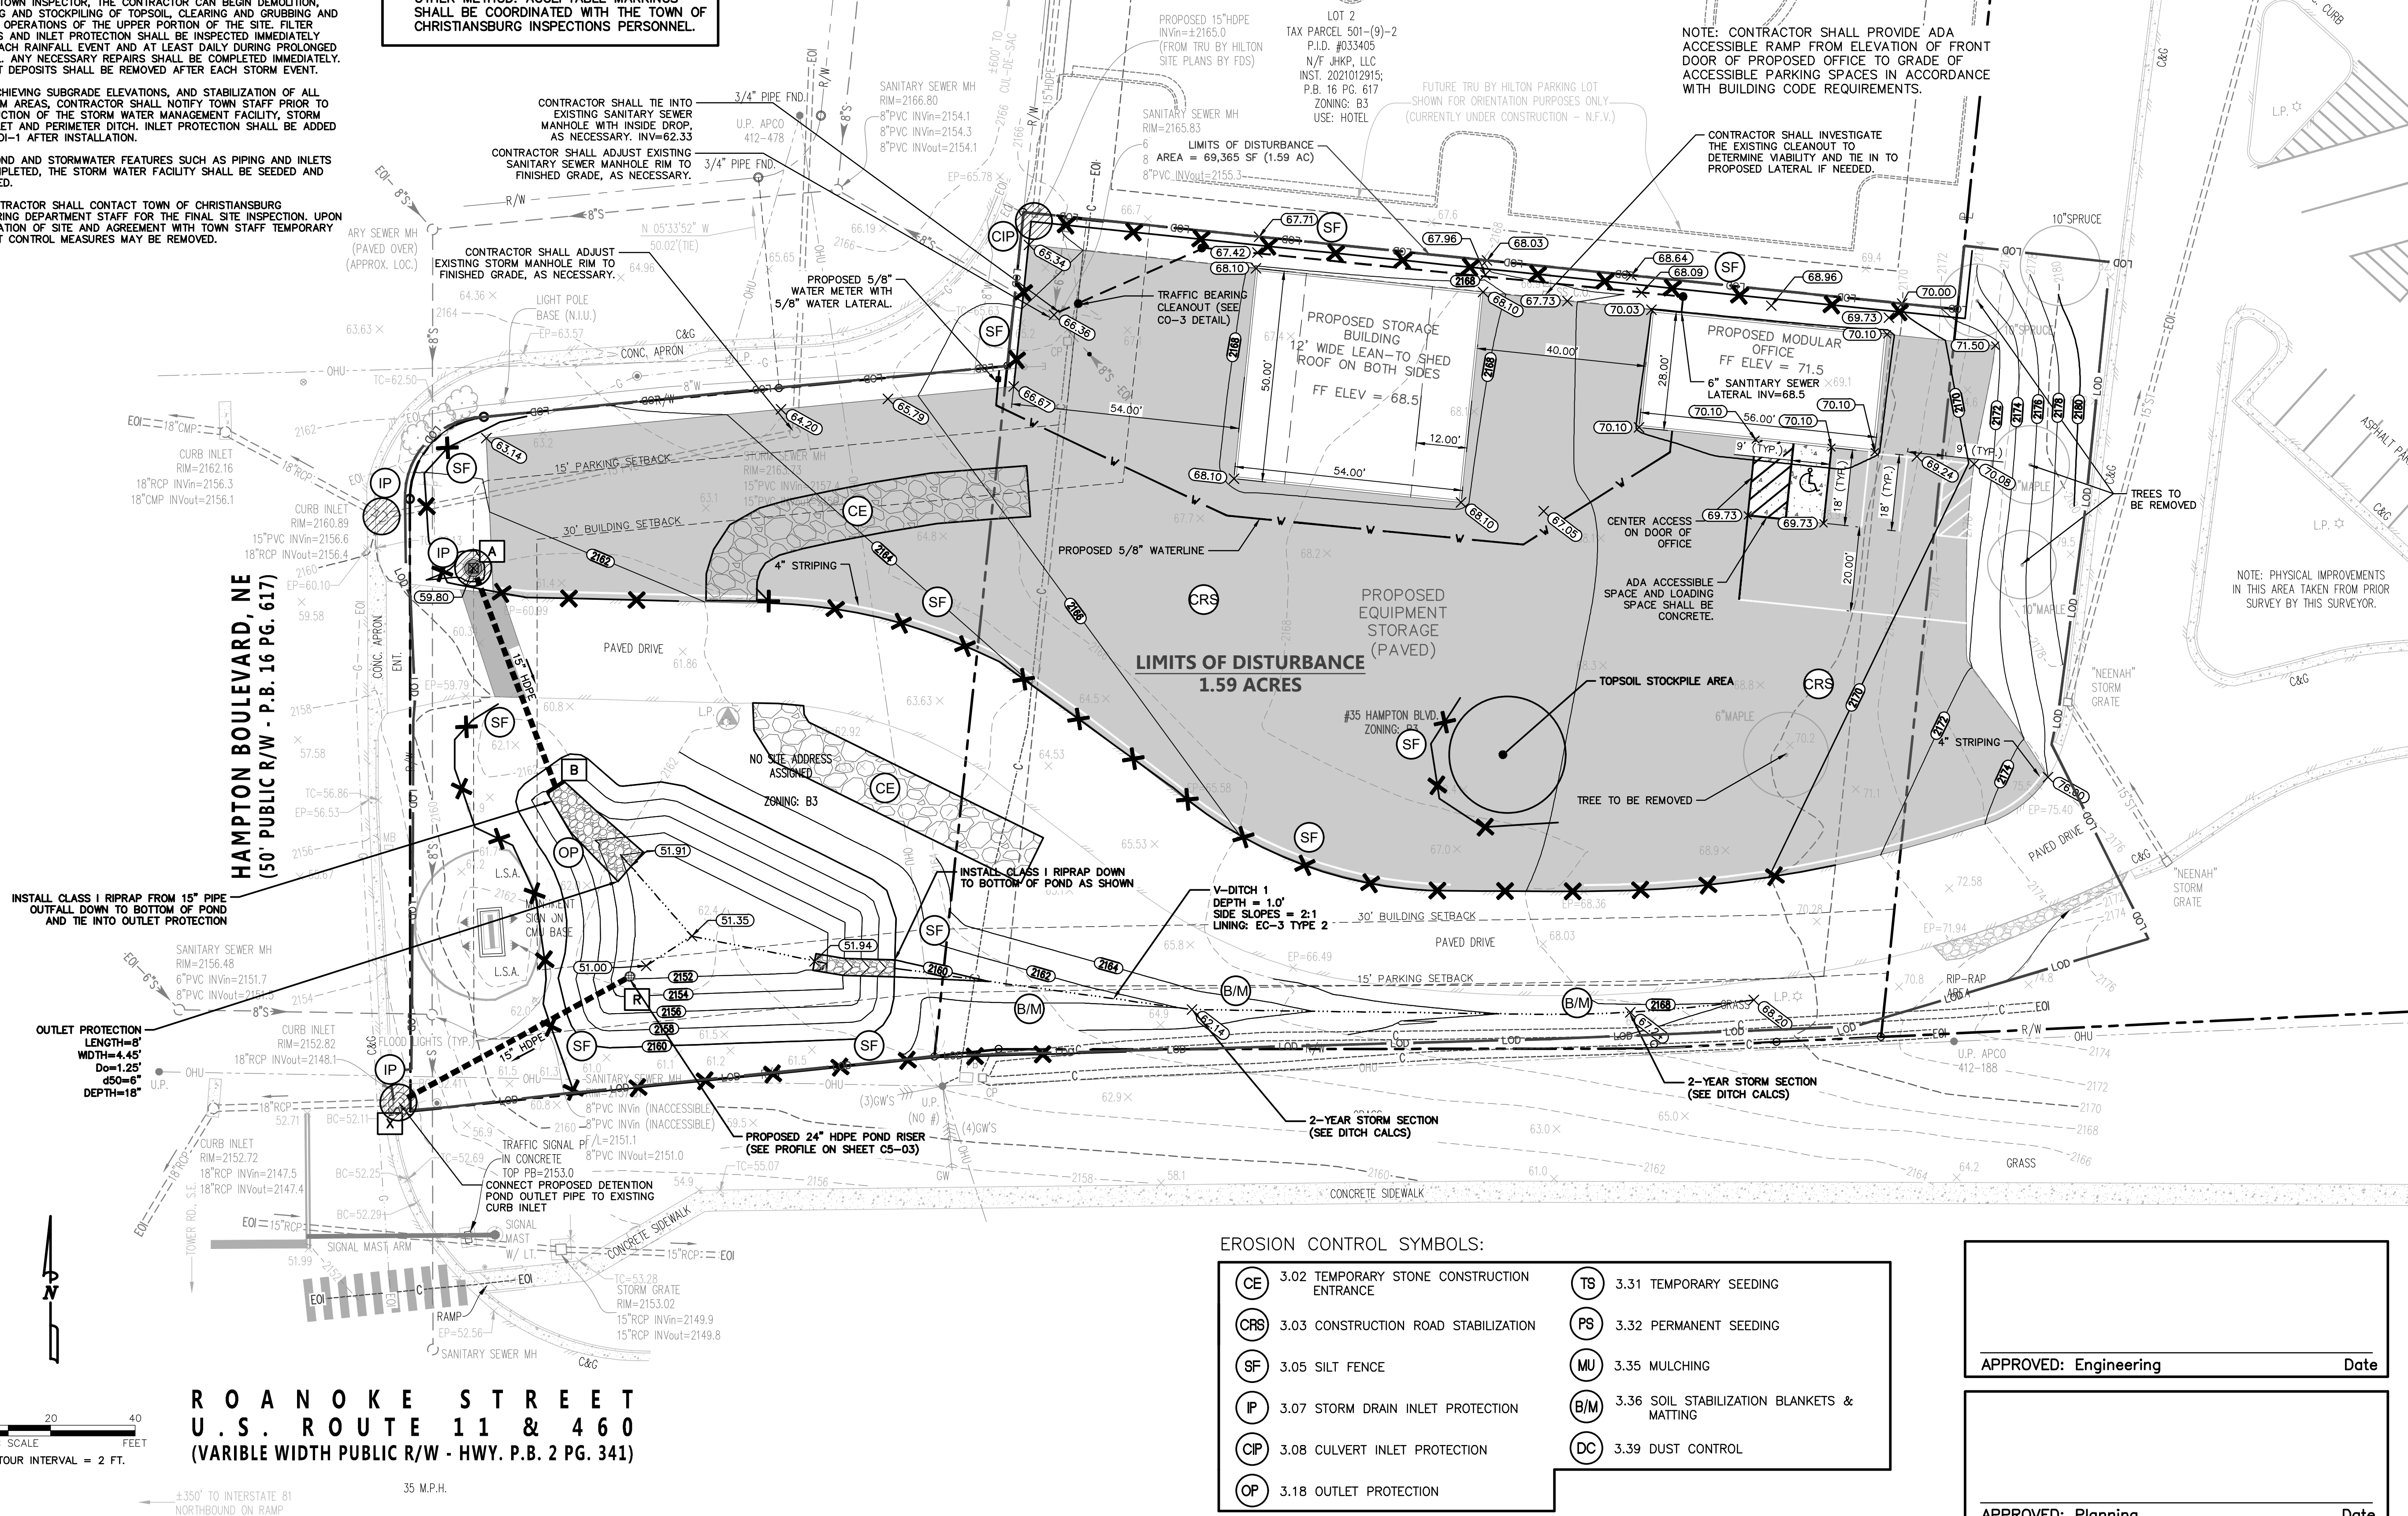

APPROVED: Engineering Date

APPROVED: Planning Date

PAVEMENT PLAN LEGEND

STANDARD ASPHALT PAVEMENT


SIDEWALK SECTIONS

FORESIGHT
DESIGN SERVICES
ENGINEERING • LAND PLANNING • SURVEYING

The drawing, design, and digital files relating to this project are the property of Foresight Design Services. The reproduction, copying, or other use of this drawing without FDS's written consent is prohibited.

POWER ZONE
EQUIPMENT STORAGE
35 HAMPTON BLVD NE

TOWN OF CHRISTIANSBURG, VIRGINIA



REVISIONS

[illegible]

PROJECT TEAM

PIC	JOHN T. NEEL, PE
PM	MATTHEW P. TOMLINSON, PE
DESIGN	ADS, C.J.L., JNY

10/01/2024

FDS JOB NO

3306

SHEET TITLE

EROSION AND SEDIMENT CONTROL PLAN

SHEET NUMBER

C5-01

X:\Drawings\3306\engineering\Design\Plans\Sheets\3306_Sht_C5_ESC_Plan_Ph1.dwg
25-01 EROSION AND SEDIMENT CONTROL PLAN 10/21/2024 10:37:31 AM Jwall AutoCAD PDF (General Documentation) p03 1-1
